



ICANN | 54

*Dublin* 

18-22 OCTOBER 2015







# IANA Stewardship Transition: Planning for Implementation


Trang Nguyen | ICANN 54 | 21 October 2015

# Agenda

- ⦿ Implementation Work and Timeline
- ⦿ Implementation Program Coordination
- ⦿ Q & A

# Implementation Work and Timeline

# Transition Timeline

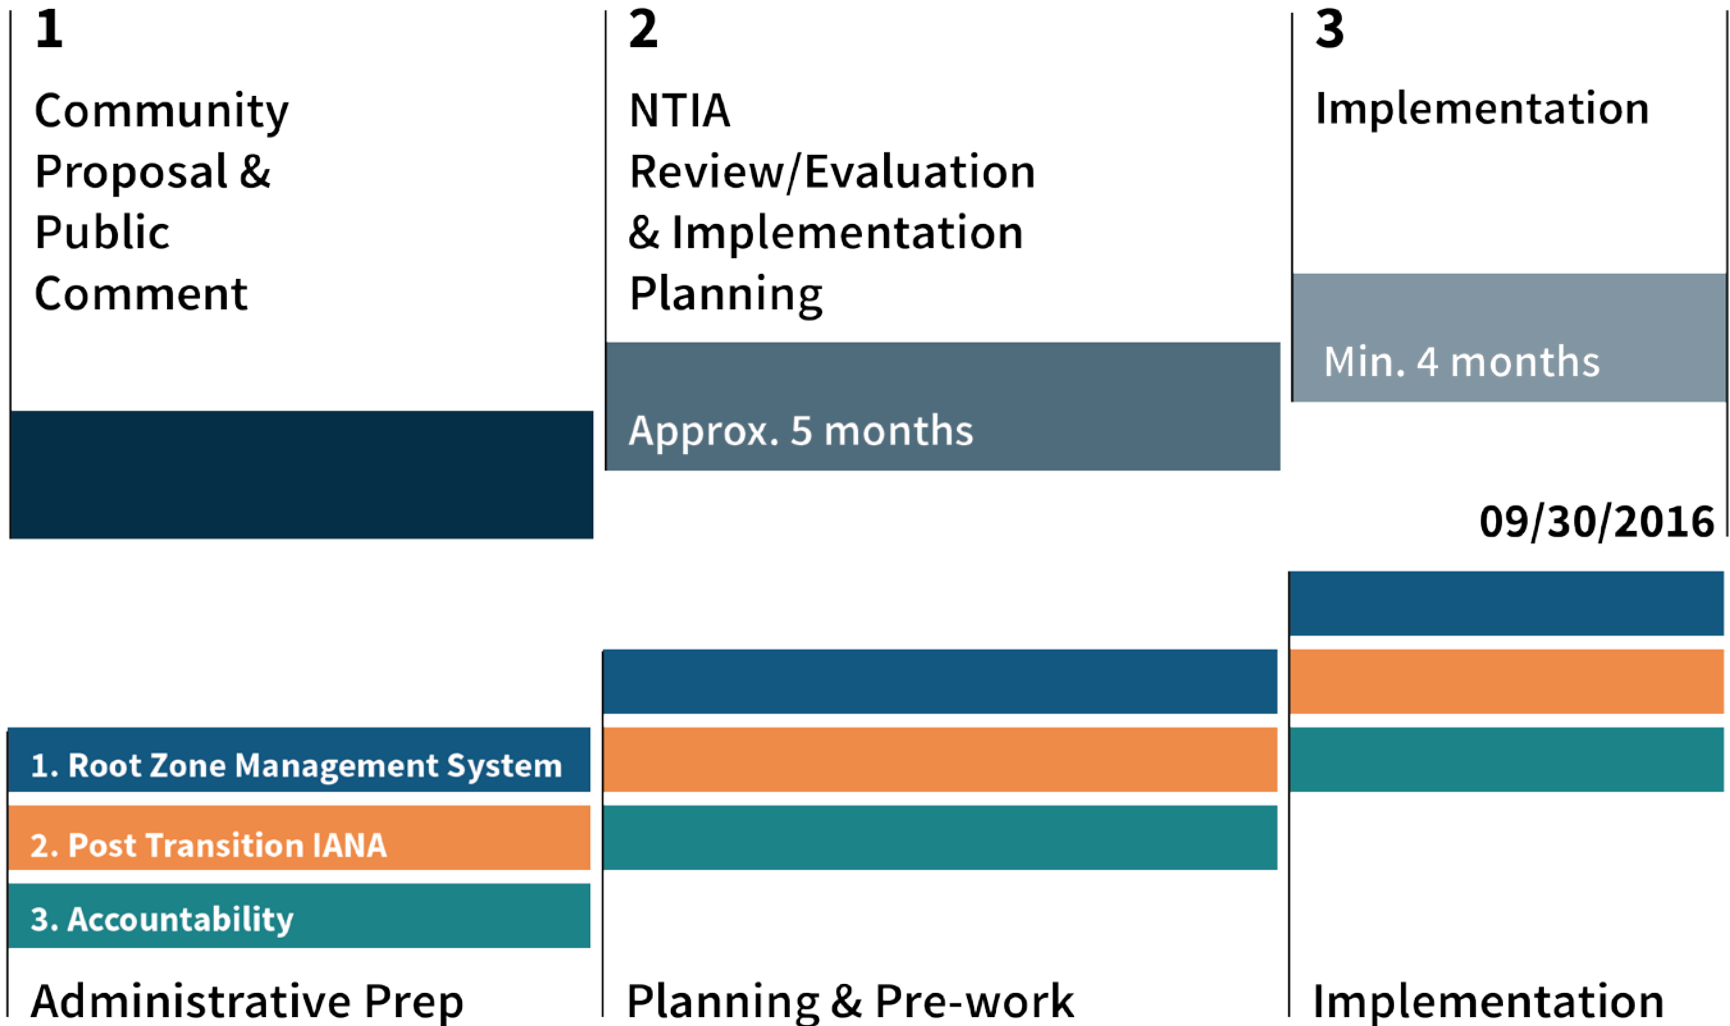



# Administrative Prep Phase

1. Identifying the projects based on the current proposal
2. Creating high level timeline
3. Engaging with community to better understand the reporting and oversight needs

# Pre-Transition Implementation Projects

1

## Root Zone Management System (RZMS)

1. RZMS changes to remove RZA role
2. Parallel testing
3. Contract with Root Zone Maintainer
4. RZMS changes to accommodate SLEs

2

## Post Transition IANA (PTI)

1. CWG-Stewardship SLAs
2. CRISP SLAs
3. Establishing PTI structure
4. Operationalizing the CSC
5. Operationalizing the RZMS Standing Committee
6. Operationalizing escalation mechanisms
7. Review and/or Document Relationships
8. Intellectual Property Rights (IPR)

3

## Accountability

1. Strengthen ICANN Governance & Accountability
2. Update of ICANN's Governance Documents

# Post-Transition Projects

1. Operationalizing IANA Function Review (IFR)
2. Operationalizing Separation Cross-Community Working Group (SCWG)
3. Study to investigate whether there is need to increase robustness of the operational arrangements for making changes to the root zone contents
4. Continuous improvement



# Implementation Timeline – Proposals Delivered in Dec. 2015


	2015			2016											
	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	
	Administrative Prep			Planning					Implementation						
RZMS changes to remove RZA role															
Parallel testing														Switch to parallel system	
Contract with root zone maintainer														RZM contract effective	
RZMS changes to accommodate SLEs															
CWG SLEs															
CRISP SLAs															
PTI structure															
CSC															
RZMS standing committee															
Escalation mechanisms															
Document relationship															
IPR															
ICANN governance & accountability															
ICANN governance documents															

# Engagement with Community

- ⊙ Administrative Prep Phase
  - ⊙ Conversations with operational communities, ICG and CCWG to better understand oversight and reporting needs
  - ⊙ Launch dedicated web page to regularly update community as appropriate throughout the administrative prep phase
- ⊙ Ongoing
  - ⊙ Visibility into status and progress of implementation
    - ⊙ Monthly webinars
    - ⊙ Updates on monthly SO/AC leader calls
    - ⊙ Bi-weekly blog posts
    - ⊙ Weekly updates on dedicated implementation web page
  - ⊙ Visibility into implementation direction
    - ⊙ Public email list
    - ⊙ Regular updates of each implementation area on dedicated implementation web page
  - ⊙ Opportunity for community input via ICANN public comment process where appropriate

# Implementation Program Coordination

# Implementation Coordination

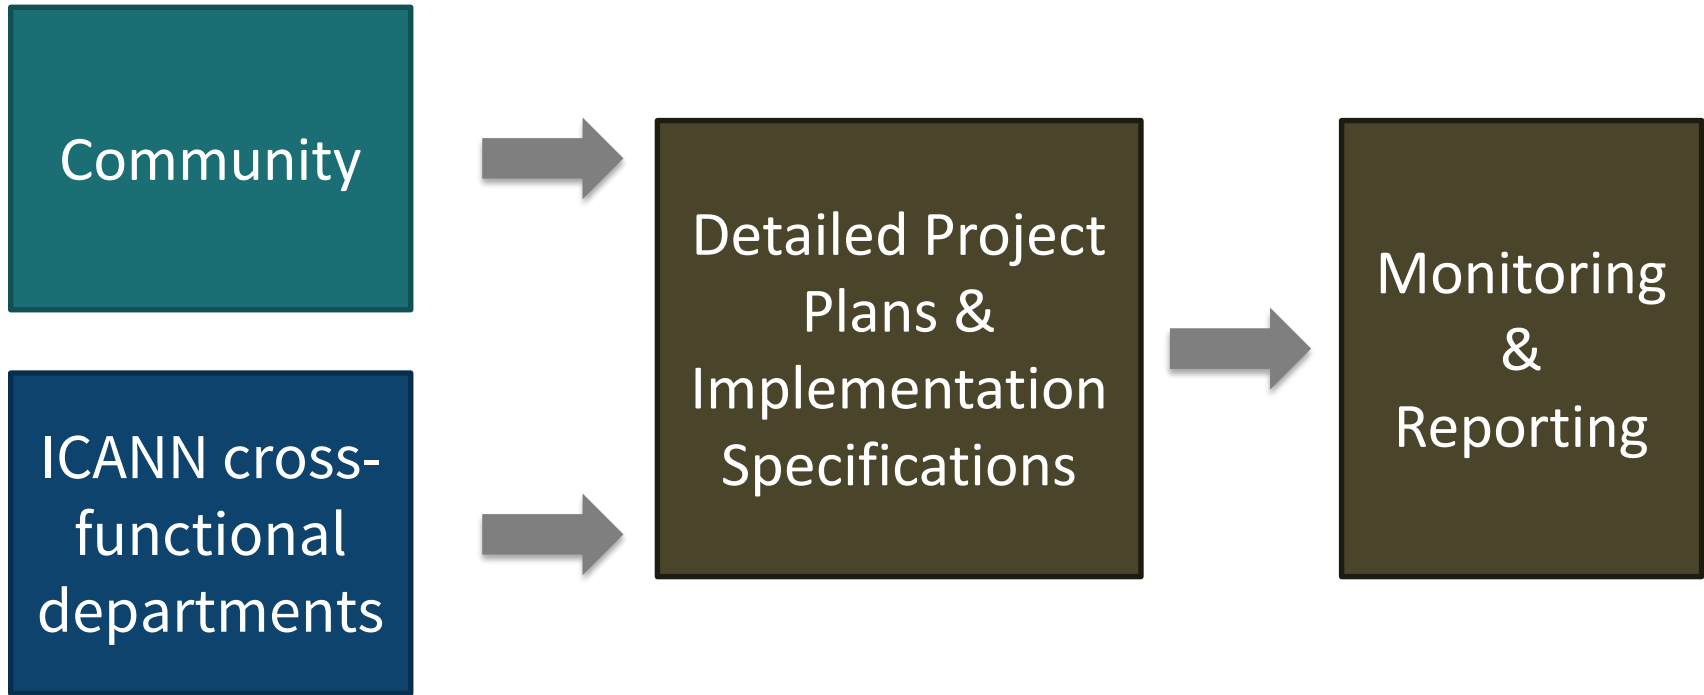

Transition Implementation Coordination Team



# Project Plans

## IANA Transition Implementation


Edit Project | Project Actions ▾

 Project Owner  
Yuko Green  
Manager, GDD Operations

Status: ● Planning    Condition: ■ On Target    Planned Completion: Dec 1, 2015    Percent Complete: 0%

Tasks   Project Details   Updates   Issues   Risks   Approvals   Legacy Gantt ▾

### IANA Transition Implementation

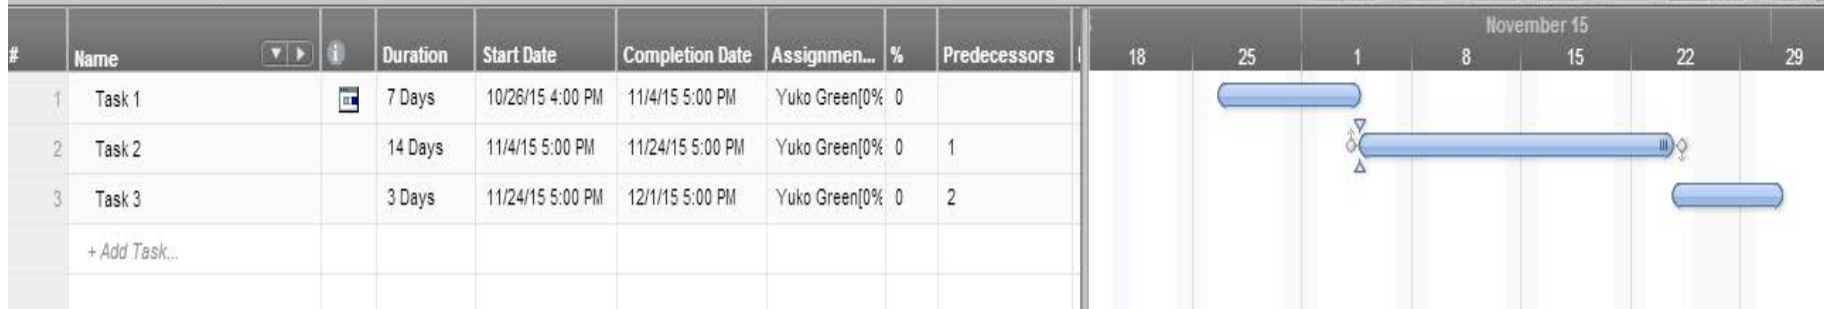

# Reporting

W

## Community Working Groups

**TBD**

- Timeline
- Status reporting
- Issues
- Implementation coordination

M

## Transition Program Facilitation Meeting

**AC / SO / NTIA / Board / WG**

- Timeline
- Status reporting
- Issues
- Budget

M

## SO-AC-SG-RALO Leaders Conference Call

**SO / AC / SG / RALO**

- Timeline
- Status reporting
- Issues
- Budget

M

## Transition Implementation Monthly Webinar

**Public**

- Status reporting
- Progress reporting
- Budget
- Current & upcoming activities

1/4 Y

## ICANN Quarterly Stakeholder Calls

**Public**

- Status reporting

OG

## Website Updates

**Public**

- Status reporting
- Progress reporting
- Budget
- Implementation related documents

W

Weekly

M

Monthly

Y

Yearly

OG

On going

# Q & A

# Questions?



## Thank You and Questions

Reach us at:

Email: [engagement@icann.org](mailto:engagement@icann.org)

Website: [icann.org](http://icann.org)



[twitter.com/icann](https://twitter.com/icann)



[gplus.to/icann](https://plus.google.com/icann)



[facebook.com/icannorg](https://facebook.com/icannorg)



[weibo.com/ICANNorg](https://weibo.com/ICANNorg)



[linkedin.com/company/icann](https://linkedin.com/company/icann)



[flickr.com/photos/icann](https://flickr.com/photos/icann)



[youtube.com/user/icannnews](https://youtube.com/user/icannnews)



[slideshare.net/icannpresentations](https://slideshare.net/icannpresentations)
